

Federal road projects under the Tinubu administration

29 May 2023 – 17 September 2026

246 documented road, bridge and maintenance entries

This compilation is the result of research conducted by **The Reality Ministry of Truth Law and Justice (TRM)**, drawing on the public sources cited in the table.

Named projects across the six geopolitical zones and the Federal Capital Territory, including works undertaken through the Federal Ministry of Works, FCTA, FERMA and regional development agencies.

Scope and reading guide

This is a public-source inventory, not a certified exhaustive national register. A record can represent a road corridor, a contract section, a bridge, or a defined maintenance intervention. Entries must not be added together as a count of distinct roads.

Every status is tied to its cited report date. An entry last documented in 2024 does not establish its present condition or completion in September 2026. Official progress claims are attributed, not independently measured.

Kilometres refer to the described contract, road, bridge or repair interval unless explicitly labelled completed. Route kilometres and carriageway-equivalent kilometres are different measures. No national kilometre total is calculated because corridors, contract sections and maintenance intervals can overlap.

Inherited projects are distinguished from new work where the evidence permits. State-only projects and roads merely inaugurated after earlier completion are not credited as new federal construction. Approval or a flag-off is not treated as proof that construction has begun.

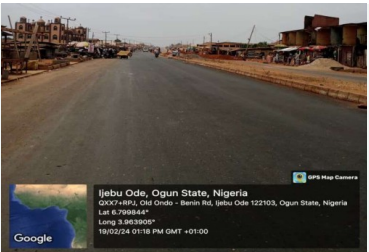
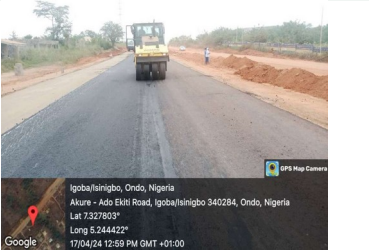
Photographs show the named segment in the cited source, often the May 2024 Ministry scorecard. They are not a current condition survey or proof of completion of the full road. Missing photographs and undisclosed lengths are stated explicitly. The companion spreadsheet retains the detailed notes and source links.

Principal records: [FMW scorecard \(27 May 2024\)](#); [FMW national update \(9 September 2026\)](#)

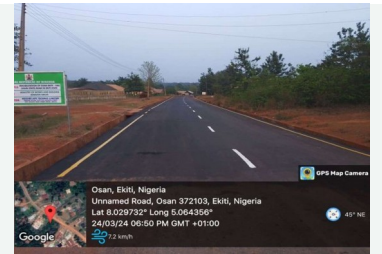
Photographic coverage: 123 entries have an embedded source photograph. Other entries identify the photographic gap.

South-West

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
1	Ifaki-Oye-Ikole-Omuo-Kogi border road: emergency repairs	20.00 km repaired critical sections; 65 km host corridor	Ekiti	Completed (100% in official May 2024 scorecard) Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Contract 8142; Oakland Construction Concept. Do not present all 65 km as repaired. Evidence: 2024-05-27 — Federal Ministry of Works	 Emergency Repairs of Ifaki-Oye-Ikole-Omuo-Kogi Border Road (F117,R543) FMW scorecard, May 2024, PDF p. 159. Capture date may be earlier.
2	Lagos-Badagry Expressway, Agbara junction-Nigeria/Benin border	46.207 km route in May 2024 scope; 92.40 carriageway-km reported	Lagos	Ongoing; 49.84% reported May 2024 Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Contract 6513; CGC; NNPC tax-credit project. Later May 2025 advance commissioning announcement says 48.6 km; this differs from the detailed scorecard. Full completion not independently confirmed. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 161. Capture date may be earlier.
3	Old Abeokuta Road, Idi Mangoro/Capitol Road junction-Post Office junction, Agege	2.30 km	Lagos	Completed (100% in official May 2024 scorecard) Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Limited rehabilitation: drainage, earthworks and asphalt; Stealth Construction. Evidence: 2024-05-27 — Federal Ministry of Works	 6 61248.3 32864.86 km 25 Jan 2024 12:59:32 pm FMW scorecard, May 2024, PDF p. 163. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
4	Ikorodu–Sagamu road rehabilitation	30.40 km main road; 1.60 km Mosimi spur separately described	Lagos and Ogun	Commissioned 31 May 2025; 91.88% in May 2024 scorecard Inherited federal project (started 2018) continued and commissioned under Tinubu Contract 6289A; Arab Contractors. Inherited project; contractor lists start in 2018. Commissioning: [source] Evidence: 2025-05-31 — State House	 FMW scorecard, May 2024, PDF p. 165. Capture date may be earlier.
5	Ijebu Ode–Ilese road, Phase II	1.00 km, Ilese-bound carriageway	Ogun	Completed (100% in official May 2024 scorecard) Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Limited rehabilitation within Ilese township; Transparent Construction. One carriageway, not both. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 167. Capture date may be earlier.
6	Akure–Ita Ogbolu–Iju–Ekiti border dualisation, Section I	18.438 km route; 36.876 carriageway-km	Ondo	Ongoing; 10.18% reported May 2024 Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Contract 7929; Samchase/Horizon JV; NNPC tax-credit scheme. Inherited 2023 award. Full corridor completion later disputed in August 2026 reporting. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 169. Capture date may be earlier.
7	Akure–Ondo road: hydraulic structures and road works, Section I	21.00 km section (CH0+000–CH21+000)	Ondo	Project documented in May 2024 scorecard; completion percentage not given Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Scorecard p170 identifies this road and section with a video rather than an extractable completion table; do not assert completed. Evidence: 2024-05-27 — Federal Ministry of Works	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
8	Ilobu-Ifon-Ilie-Erinle road	44.00 km project; only 7 km completed alleged by community in June/July 2025	Osun and Kwara	Continued; officially commissioned May 2025, but full-completion claim disputed Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Sukuk contract 6620; IAC Technical. 19% in May 2024. Presidency lists commissioning; community petition says only 7 of 44 km finished: [source] . Do not describe 44 km as fully completed. Evidence: 2025-07-07 — punchng.com	 FMW scorecard, May 2024, PDF p. 172. Capture date may be earlier.
9	Ife-Ifetedo-Ondo border road: flood intervention	0.85 km intervention within CH0+000–CH2+000	Osun	Completed (100% in official May 2024 scorecard) Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Hot Construction; length is treated portion, not entire named road. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 174. Capture date may be earlier.
10	Ibadan-Oyo dual carriageway rehabilitation, Section I	43.00 km route; 86.00 carriageway-km	Oyo	Work documented in May 2024; minister described project as abandoned in July 2025 Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Contract 7644; Arab Contractors; Sukuk funded. Distinct from Oyo–Ogbomoso section. May 2024 progress is historical. Minister described project as abandoned and sought funds 27 July 2025: [source] . No full-completion evidence. Evidence: 2025-07-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 177. Capture date may be earlier.
11	Deep-Sea Port access road via Epe to Sagamu-Benin Expressway	54.24 km combined route: Section 1 26.74 km; Section 3 27.50 km	Lagos and Ogun	Commissioned 31 May 2025; sections were ongoing May 2024 Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Contract 6993C; Dangote tax-credit project, Hitech works. Section 1 dual carriageway reported as 53.48 carriageway-km. Contractor continues to label archive ongoing; commissioning is the presidential report: [source] Evidence: 2025-05-31 — State House	 FMW scorecard, May 2024, PDF p. 180. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
12	Ekiti border-Ikere-Ado Ekiti road, Section II	21.272 km route; 42.544 carriageway-km	Ekiti	Ongoing; 1.46% reported May 2024 Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Contract 7930, Kopek; new dualisation to Ikere plus rehabilitation of existing dualised Ikere-Ado section. Correct chainage 18+438 to 39+710; printed heading 139+710 is a typo contradicted by body. Inherited 2023 award. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 182. Capture date may be earlier.
13	Molege-Elegbeka-Ifon road repairs, Section II	6.00 km (CH66+000– CH72+000)	Ondo	Completed (100% in official May 2024 scorecard) Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Ladeen Global Resources; special/emergency repairs. Photo p184 is captioned ongoing and is evidence of works, not date-specific completion. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 184. Capture date may be earlier.
14	Ikirun-Eko Ende road: flood intervention	0.90 km intervention; 4.00 km host section	Osun	Completed (100% in official May 2024 scorecard) Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Expert Edge Contractor; do not present 4 km host section as repaired length. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 186. Capture date may be earlier.
15	Osan Ekiti-Ora road repairs	1.25 km intervention; 8.30 km host road	Ekiti-Osun	Completed (100% in official May 2024 scorecard) Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here APS Techno; emergency repair. Do not report all 8.3 km as completed. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 188. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
16	Iddo Bridge: substructure and underwater repairs	0.534 km project length; body describes 0.525 km bridge	Lagos	Ongoing; 13% reported May 2024 Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Julius Berger. The scorecard has a 9 m internal length discrepancy; retain stated project length with note. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 224. Capture date may be earlier.
17	Olomi Bridge and ramps rehabilitation (Route 20/A1)	Not stated in source	Oyo	Completed (100% in official May 2024 scorecard) Federal Ministry of Works intervention recorded during Tinubu's tenure; original contract date not established here Contract 8514 awarded 12 January 2024 to Ben Daniels Global Impex; scarification, asphalt surfacing of ramps and debris clearance. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 245. Capture date may be earlier.
18	Apapa-Oworonshoki-Ojota-Oshodi Expressway	36.02 km route	Lagos	Reconstructed road commissioned 26 May 2024 Inherited federal/Dangote tax-credit project completed/commissioned under Tinubu Concrete pavement, four sections; Dangote Industries with Hitech subcontractor. Evidence: 2024-05-26 — State House	Verified segment photograph not available.
19	Third Mainland Bridge: carriageway, expansion-joint and associated structural rehabilitation	11.80 km bridge; rehabilitation rather than new bridge	Lagos	Main rehabilitation reopened April 2024 and commissioned 26 May 2024; underwater intervention remained a separate issue in September 2026 Federal rehabilitation of existing bridge under Tinubu 2024 commissioning confirmed by [source] . May 2024 scorecard separately records underwater repairs at 19.17%; Sept 2026 source says intervention on defective underwater elements still being determined. Do not imply every structural issue resolved. Evidence: 2026-09-09 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 220. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
20	Carter Bridge: underwater repairs and replacement bridge works	Not stated in source	Lagos	Weekly underwater maintenance continuing; replacement bridge construction commenced by 9 September 2026 New replacement project plus federal repairs under Tinubu New bridge site handed over to CCECC; May 2024 scorecard records earlier Julius Berger underwater repairs at 15%. Photo p226 shows earlier repair phase, not the new replacement. Evidence: 2026-09-09 — Federal Ministry of Works	 Mar 26, 2024 at 3:06:07 PM Carter Bridge Mainland Lagos Nigeria FMW scorecard, May 2024, PDF p. 226. Capture date may be earlier.
21	Eko Bridge: comprehensive repairs from Alaka/Surulere to Apongbon, including ramps	4.10 km	Lagos	Commissioned 31 May 2025 Federal emergency rehabilitation under Tinubu Existing bridge repairs; not a newly constructed 4.1 km bridge. Evidence: 2025-05-31 — State House	Verified segment photograph not available.
22	Lagos-Sagamu-Ibadan Expressway, Section II (Sagamu-Ibadan)	166.8 carriageway-km in May 2025 commissioning schedule; not 166.8 route-km	Ogun and Oyo	Commissioned 31 May 2025; residual 8.5 km works inspected July 2025 Inherited project continued and commissioned under Tinubu RCC. Commissioning is confirmed by [source] scope figure in [source] . Commissioning does not mean no outstanding works. Evidence: 2025-07-06 — independent.ng	Verified segment photograph not available.
23	Lagos-Ibadan Expressway: flood-damaged section intervention	Not stated in source	Lagos-Ogun-Oyo corridor; exact affected location not specified	Work commenced by 9 September 2026 New emergency intervention under Tinubu on existing expressway Separate 2026 emergency operation on the same corridor; do not add to total route length. Evidence: 2026-09-09 — Federal Ministry of Works	Verified segment photograph not available.
24	Sagamu-Ore road: concrete reconstruction package	96 km package; 48 km concrete completed reported September 2026	Ogun and Ondo	Ongoing; partly completed Inherited federal corridor continued/redesigned under Tinubu Source separately mentions a 24 km section near Ore abandoned by previous contractor and orders restoration; do not count that order as completed works. Route/carriageway basis of quoted 96 km is not expressly stated. Evidence: 2026-09-09 — Federal Ministry of Works	Verified segment photograph not available.
25	Ibadan-Ife-Ilesa expressway reconstruction	108 km contract section; about 70 km work reported June 2026, basis not specified	Oyo and Osun	Ongoing; temporarily paused for pavement-mixture review June 2026; resumption reported 6 July 2026 Existing federal road rehabilitation/reconstruction continued under Tinubu CBC Global. June inspection and figures: [source] . Some works still needed shoulders; 70 km is not a certificate of complete project delivery. Evidence: 2026-07-06 — thenationonlineng.net	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
26	Oyo-Ogbomoso dual carriageway	52 km remaining contract referenced in January 2026 reporting; 86 km also quoted in July inspection report—scope basis requires reconciliation	Oyo	Ongoing; delays reported January 2026; September 2026 deadline was a target Inherited federal project re-awarded and continued under Tinubu New contractor JRB; prior RCC contract terminated. Do not assume completion because deadline has arrived. July 2025 report [source] quotes 86 km. Evidence: 2026-01-24 — punchng.com	Verified segment photograph not available.
27	Lagos-Calabar Coastal Highway, Phase I Section I: Ahmadu Bello Way/Eko Atlantic-Eleko	47.47 km package; 30 km opened/commissioned segment documented	Lagos	Partly opened; construction package continued; full completion not verified in retrieved sources New federal construction begun March 2024 under Tinubu Contractor cites December 2025 ministry milestone and Q2 2026 full-delivery target; target is not completion. Part commissioned 31 May 2025. Do not claim 700/750 km entire corridor built. Photograph is an official May 2024 construction-stage segment, not evidence of the full corridor being completed. Evidence: 2025-12-13 — hitech-company.com	 FMW scorecard, May 2024, PDF p. 211. Capture date may be earlier.
28	Lagos-Calabar Coastal Highway, Phase I Section II	55.6 km package per contractor's ministry-based description	Lagos, Epe corridor	Under construction; inspected 19 June 2026 New federal construction under Tinubu FMW article dated June20 reports minister inspection at Section2 Epe June19. Length source: [source] . The two Lagos packages total approximately 103 km, not extra 103 km in addition. Evidence: 2026-06-20 — Federal Ministry of Works	Verified segment photograph not available.
29	Lagos-Calabar Coastal Highway: Ogun construction section	28 km route; ministry says dual carriageway ('by two')	Ogun	Under construction as of 5 August 2026 inspection update New federal construction under Tinubu Construction length quoted by minister; not completed length. Do not confuse this with older proposed Ogun total alignment. Evidence: 2026-08-06 — Federal Ministry of Works	Verified segment photograph not available.
30	Lagos-Calabar Coastal Highway: Ondo Section 4B	52 km route; ministry says dual carriageway ('by two')	Ondo	Under construction; inspected 5 August 2026 New federal construction under Tinubu Not the entire planned Ondo coastal alignment; no completion claim. Evidence: 2026-08-06 — Federal Ministry of Works	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
31	Sango-Ota-Idiroko road reconstruction, Section I	14 km revised Section I; 0.509 km flyover separately listed	Ogun	Construction ongoing June 2025; scope/design revised November 2025 Federal reconstruction continued under Tinubu Actual construction corroborated by [source] (17 June2025); Laralek. Revised concrete scope is not a completion claim. Evidence: 2025-11-06 — allafrica.com	Verified segment photograph not available.
32	Obelle-Ilaro-Papalanto-Sagamu road reconstruction	100.50 km project	Ogun	Ongoing construction reported 24 January 2026 Inherited federal/Dangote tax-credit project continued under Tinubu May2024 scorecard lists project as about to commence; governor's 2026 update confirms subsequent ongoing works. Not a state-only project; Dangote tax credit. Evidence: 2026-01-24 — facebook.com	Verified segment photograph not available.
33	Lagos-Sagamu Expressway: outstanding dual-carriageway works and flyovers	12 km route; 24 carriageway-km, plus flyovers	Lagos and Ogun	Ongoing in July 2025 Inherited federal project continued under Tinubu CBC contractor. Residual works package within Lagos-Ibadan corridor, not 12 additional kilometres of new national road. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.

South-East and South-South



S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
34	Enugu-Onitsha Expressway rehabilitation and concrete reconstruction	107 route-km (dual carriageway; corridor scope)	Enugu and Anambra	Reconstruction ongoing; reopening deadline announced for 31 March 2026 Inherited; continued and rescope under Tinubu The separate 72-km descope concrete contract is a component of this corridor, not an extra 72 route-km. Deadline is not proof of completion. Evidence: 2026-03-24 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 149. Capture date may be earlier.
35	Abakpa Junction interchange	Not stated	Enugu	Under construction at ministerial inspection Federal works under Tinubu; initiation date not established CCECC; junction facility within Enugu-Onitsha corridor, not additional corridor kilometres. Evidence: 2025-09-27 — Federal Ministry of Works	Verified segment photograph not available.
36	Eke-Obinagu Junction flyover and dual service roads	0.345 bridge-km; 1.05 km dual service road	Enugu; Enugu-Abakaliki road junction	Under construction at inspection Federal works under Tinubu; initiation date not established 23-span flyover; Reinforced Global Resources. Bridge and service-road lengths must remain separate. Evidence: 2025-09-27 — Federal Ministry of Works	Verified segment photograph not available.
37	Enugu-Abakaliki road rehabilitation	36 km (reported contract scope)	Enugu-Ebonyi corridor	Listed as ongoing Inherited/continued federal intervention Contractor: Reinforced Global Resources. This is the named contract length, not all kilometres newly completed. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
38	Enugu-Lokpanta, Enugu-Port Harcourt Expressway Section III	61 route-km (dual carriageway)	Enugu-Lokpanta corridor	Ongoing; ministry also listed continuing works July 2025 Inherited federal project continued Length independently stated on 2024 scorecard p150. Photos are historical May2024 progress. Evidence: 2025-07-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 151. Capture date may be earlier.
39	Umuahia Tower-Aba rail/road crossing, Enugu-Port Harcourt Expressway Section II	56 km (contract scope reported)	Abia	85% overall completion reported at October 2025 inspection Inherited federal project continued Arab Contractors; percentage is overall project progress, not solely work since May2023. Evidence: 2025-10-20 — Federal Ministry of Works	Verified segment photograph not available.
40	Aba-Port Harcourt, Enugu-Port Harcourt Expressway Section IV	43 km (contract scope)	Abia and Rivers	Works ongoing but deficient; Port Harcourt-bound work descope and termination warning issued Inherited federal project continued/rescoped Report documents poor construction and failure; cannot describe entire road as completed. Evidence: 2025-10-20 — Federal Ministry of Works	Verified segment photograph not available.
41	Second Niger Bridge access road Phase 2A, Delta side	17 km (July2025 scope; earlier scorecard 17.75 km)	Okpanam/Asaba-Oko, Delta	Ongoing access-road construction Inherited access-road contract continued/re-awarded CCECC under updated scope. Main Second Niger Bridge was commissioned before Tinubu; this row is access road only. Earlier length differs. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
42	Second Niger Bridge access road Phase 2B, Anambra side	17.5 km (July2025 scope; earlier scorecard 17.71 km)	Obosi-Onitsha-Enugu Expressway, Anambra	Ongoing access-road construction Inherited access-road contract continued/re-awarded CGC under updated scope. Main bridge excluded. Earlier length differs. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
43	Bodo–Bonny road and bridges	37.9 km contractor specification (approximately 38 –39 km)	Rivers; Bodo to Bonny Island	Described as recently completed by ministry April2026 Inherited; completed under Tinubu with NLNG partnership Contractor specification: [source] . Extension approved April2026 is separate and not treated as built. Evidence: 2026-04-29 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 231. Capture date may be earlier.
44	Eleme Junction–Onne Port Junction, East–West Road Section IIIA, including Aleto bridge works	15 route-km (30 carriageway-km)	Rivers	One carriageway commissioned by Sep2025; remaining bridges/second phase under work March2026 Inherited project redesigned and continued under Tinubu May2026/Aug2026 deadlines were forecasts, not verified completion. 15- km route confirmed scorecard p198 and FMW /read/3336. Evidence: 2026-03-22 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 199. Capture date may be earlier.
45	Eket bypass (East–West Road Section IV addendum)	9.75 km (scorecard); 9.7 km rounded in 2025 update	Akwa Ibom	Ongoing in July2025 update Inherited federal project continued Do not describe all 9.75 km as completed; dualisation scope. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
46	East–West Road Section II, Kaiama– Ahoada–Port Harcourt works	Not stated in cited progress update	Bayelsa and Rivers	Ongoing Inherited federal project continued Setraco; Section II includes phases. Separate Eleme–Onne project is not included in this row. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
47	Nembe–Brass road project	Not stated in cited progress update	Bayelsa	Listed as ongoing Federal works under Tinubu; precise initiation not established Do not substitute length of state-funded Nembe–Brass sections or Yenegwe corridor without matching contract boundaries. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
48	Lagos–Calabar Coastal Highway, initial Cross River/Akwa Ibom construction sections	65 route-km combined ongoing scope (July2025)	Cross River and Akwa Ibom	Under construction New Tinubu administration project 65 km is combined ongoing scope, not completed length; avoid adding this to an entire 700/750-km corridor total. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
49	Calabar–Ebonyi–Benue–Abuja / Trans-Saharan Highway, Ebonyi section	Length unresolved: official update uses conflicting 118 / 123.64 / 231.64-km descriptions	Ebonyi toward Benue border	Construction reported ongoing; scope expanded New Tinubu administration project Source mixes single/dual-carriageway measures and internally inconsistent figures. No defensible single route length assigned. Evidence: 2025-08-04 — Federal Ministry of Works	Verified segment photograph not available.
50	Afikpo–Abia–Imo road works	Not stated	Ebonyi, Abia and Imo	Ongoing works reported; individual contracts and lengths not identified Inherited/continued federal intervention Broad corridor name only; exact contract boundaries not published in cited update. Treat as corridor record, not quantified completed length. Potential overlap with named regional road sections; this is an inventory entry, not an independently measurable or additive road length. Evidence: 2025-08-04 — Federal Ministry of Works	Verified segment photograph not available.
51	Onitsha–Owerri–Aba corridor works	Not stated	Anambra, Imo and Abia	Ongoing works reported; individual contracts and lengths not identified Inherited/continued federal intervention Broad corridor report; possible overlap with separately documented Oba junction/interventions. Do not total kilometre lengths. Potential overlap with named regional road sections; this is an inventory entry, not an independently measurable or additive road length. Evidence: 2025-08-04 — Federal Ministry of Works	Verified segment photograph not available.
52	Benin–Asaba reconstruction / emergency rehabilitation	225 km concession corridor; emergency repair length unreported	Edo and Delta	PPP work reported started Aug2025; emergency restoration and redesign directed Sep2026 Inherited concession; works and intervention during Tinubu administration 225-km scope and work start: [source] . Emergency instruction is not proof entire length rehabilitated. Earlier Benin–Agbor spot repairs overlap geographically. May2024 scorecard also reports completed spot repairs on the Benin–Agbor segment (70.4-km host corridor; actual repaired length not stated). The photo is historical May2024 evidence of that segment, not September2026 condition. Evidence: 2026-09-09 — Federal Ministry of Works ; Additional source	 FMW scorecard, May 2024, PDF p. 207. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
53	Summit Junction-First Niger Bridge approach road rehabilitation	11.5 route-km (23 carriageway-km)	Asaba, Delta	Concrete rehabilitation ongoing September 2026 Tinubu-era emergency intervention on existing road Length and emergency award reported 7 Aug 2025: [source] . Excluded from 225-km concession length in that source. Evidence: 2026-09-09 — Federal Ministry of Works	Verified segment photograph not available.
54	First Niger Bridge structural rehabilitation	Not stated; bridge intervention	Asaba-Onitsha, Delta/Anambra	Bridge closed; contractor mobilised and comprehensive rehabilitation started Tinubu-era rehabilitation of existing bridge Bridge rehabilitation, not a new bridge. Evidence: 2026-09-09 — Federal Ministry of Works	Verified segment photograph not available.
55	Achingali-Udoobi-Udo-Na-Umu Uwana-Ubakala road and bridge	21 km plus bridge	Imo	Ongoing; 31% overall progress stated Inherited federal project continued Detailed scorecard p136; contractor Boliv. Project percentage is cumulative. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 137. Capture date may be earlier.
56	Aba-Ikot Ekpene dualisation	37 route-km	Abia and Akwa Ibom	Ongoing; 15.87% overall progress in detailed project page Inherited federal project continued p138. Summary table reports 2.03%, conflicting with detailed page; no claim of kilometres completed. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 139. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
57	Umuahia-Umudike-Ikwuano-Ikot Ekpene rehabilitation	48.92 km project field; 48.29 km description (source conflict)	Abia and Akwa Ibom	Ongoing; contractor on site Inherited federal project continued Detailed p140 reports 74.57%, summary table 11.91%. Length/progress discrepancy requires reconciliation; no completed-km claim. Evidence: 2024-05-27 — Federal Ministry of Works	
58	Oba-Nnewi-Arondizuogu-Okigwe: two outstanding sections	38.50 km contract within 76.5-km corridor	Anambra and Imo	Ongoing; 14.60% overall progress Inherited federal project continued Project page p142. Scope is two outstanding sections, not the entire route. Evidence: 2024-05-27 — Federal Ministry of Works	
59	Old Enugu-Onitsha road via Opi-Ukehe-Okpatu-Abor-Udi-Oji, with spurs	90 km including spurs	Enugu to Anambra border	Ongoing; contractor on site Inherited federal project continued Distinct old single-carriageway alignment, not Enugu-Onitsha Expressway. Detailed scorecard p144. Evidence: 2024-05-27 — Federal Ministry of Works	
60	Abakaliki-Oferekpe road intervention	1.4 km project field (title chainage 4-7 km inconsistent)	Ebonyi	Reported completed in scorecard Federal construction completed during reporting period; initiation not established p146: 100% reported. Numerical inconsistency explicitly preserved rather than inventing corrected length. Evidence: 2024-05-27 — Federal Ministry of Works	

FMW scorecard, May 2024, PDF p. 141. Capture date may be earlier.

FMW scorecard, May 2024, PDF p. 143. Capture date may be earlier.

FMW scorecard, May 2024, PDF p. 145. Capture date may be earlier.

FMW scorecard, May 2024, PDF p. 147. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
61	Trans Ekulu township roads limited rehabilitation	2.0 km project field; 3.5 km title (source conflict)	Enugu	Intervention documented; completion status contradictory Federal rehabilitation under Tinubu reporting period p152 says 12.5% and also 'project completed'; cannot responsibly classify as fully complete. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 153. Capture date may be earlier.
62	Ugep-Ediba-Itigidi-Adadama-Ekureku-Abaomege limited rehabilitation	0.65 km intervention within 27-km route	Cross River and Ebonyi	Ongoing; 92% overall progress Tinubu-era special intervention Detailed emergency-project page155. Do not treat entire27-km road as rebuilt. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 156. Capture date may be earlier.
63	Benin-Sapele-Warri Section I: Benin City-Imasabor	28.275 route-km	Edo	Ongoing reconstruction Inherited federal project continued Detailed p190; chainage0+000-28+275; Levant Nigeria. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 191. Capture date may be earlier.
64	Benin-Sapele-Warri Section III: Ibada Elume-Warri	23.20 route-km	Delta	Ongoing reconstruction Inherited federal project continued Detailed p192; chainage66+800-90+000; SKECC Nigeria. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 193. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
65	Sapele-Agbor dualisation, Sapele-Ewu Section I	110.63 km	Delta	Ongoing dualisation Inherited federal project continued Detailed p195; Amukpe near Sapele to Benin-Asaba Expressway at Agbor; CGC. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 196. Capture date may be earlier.
66	Calabar-Itu-Odukpani dualisation, Odukpani-Okuiboku section	28.6 km contract scope	Cross River / Akwa Ibom corridor	Ongoing; 48.98% overall progress in detailed page Inherited federal project continued p200; Sermatech, contract7006. Summary names same contract Oku Iboku -Power Plant; treat as one contract pending boundary reconciliation. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 201. Capture date may be earlier.
67	Kaa-Wiagara-Beri-Taabah-Umuagbai road rehabilitation	2.00 km intervention within 34-km route	Rivers	Ongoing; 60% overall progress Tinubu-era special intervention Detailed p202. Special intervention, not reconstruction of all34km. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 203. Capture date may be earlier.
68	Benin bypass limited rehabilitation of failed sections	Repair length unreported; 45.8-km corridor	Edo; Oluku to Sapele interchanges	Limited repair project reported completed Federal repair project completed during reporting period p204 quotes45.8km for road; work expressly limited to critically failed spots. Not45.8km wholly rebuilt. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 205. Capture date may be earlier.


S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
69	Aleki Bridge failed-section rehabilitation, Emohua-Buguma-Degema road	Not stated; bridge intervention	Rivers	Before/during/after photographic record in scorecard Federal bridge repair during reporting period Page246 is photographic evidence; no detailed completion certificate or intervention length. Evidence: 2024-05-27 — Federal Ministry of Works	

FMW scorecard, May 2024, PDF p. 246. Capture date may be earlier.

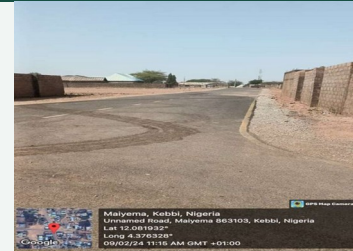
North-West


S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
70	Abuja-Kaduna-Zaria-Kano highway: Infioquest Lot 1	118 km reported lot length; carriageway basis requires care	FCT / Kaduna; Abuja-Kaduna corridor	Reported completed, predominantly in concrete, by 9 September 2026 Inherited corridor; outstanding works reprocured/continued under Tinubu Do not add to overall corridor length. FMW 1 May 2026 separately reported a completed 108-km Tungan-Maje-Jere stretch; inconsistent section measures prevent treating this as unqualified route-km. [source] Evidence: 2026-09-09 — Federal Ministry of Works	Verified segment photograph not available.
71	Abuja-Kaduna-Zaria-Kano highway: Infioquest Lot 2	82 route km / 164 carriageway-km	Kaduna; Jere-Kaduna outstanding works	Over 60% complete; construction ongoing Inherited corridor; continued/reprocured under Tinubu Length basis expressly clarified as 82 × 2 in FMW 10 October 2025: [source] . December 2026 was a target, not achieved completion. Evidence: 2026-09-09 — Federal Ministry of Works	Verified segment photograph not available.
72	Sokoto-Badagry Superhighway: Sokoto section	120 km contracted/under construction	Sokoto State; Illela axis	Construction ongoing as reported July 2025 New construction initiated under Tinubu on long-proposed corridor Part of planned 1,068-km corridor; never count 1,068 km as completed. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
73	Sokoto-Badagry Superhighway: Kebbi sections 2A and 2B	About 258 km reported state section; 19 km concrete pavement recorded	Kebbi State	2A reported 40%; 2B 16%; earthworks and paving ongoing New construction initiated under Tinubu Release also gives chainage 120-385 (=265 km), inconsistent with reported 258 km; retain approximation and disclose discrepancy. 19km pavement is not completion of all road elements. Evidence: 2026-05-08 — State House	Verified segment photograph not available.
74	Zaria-Funtua-Sokoto dualisation, Section I: Zaria-Funtua-Shema	87.575 km project length	Kaduna / Katsina	5% recorded in May 2024 scorecard; corridor still ongoing in September 2026 Inherited; continued under Tinubu Contract 8025, Mothercat. Latest corridor-wide status: [source] ; no updated section-specific percentage verified. Evidence: 2024-05 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 104. Capture date may be earlier.

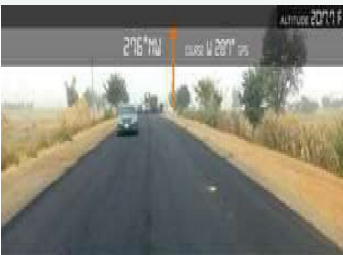
S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
75	Zaria-Funtua-Sokoto dualisation, Section II: Shema-Tsafe-Gusau	86.1 km project length	Katsina / Zamfara	3.60% in May 2024 scorecard; corridor still ongoing in September 2026 Inherited; continued under Tinubu Contract 8026, Setraco. Latest corridor-wide status: [source] . Evidence: 2024-05 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 106. Capture date may be earlier.
76	Zaria-Funtua-Sokoto dualisation, Section IV: Talata Mafara-Sokoto City	105.442 km project length	Zamfara / Sokoto	3.41% in May 2024; September 2026 release reports over 50 km of one carriageway completed from Sokoto towards Zamfara Inherited; continued/redesigned under Tinubu Section length from scorecard p107, contract 8028. 50km is one-carriageway work, not 50km of completed dual carriageway. Evidence: 2026-09-09 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 109. Capture date may be earlier.
77	Kano Northern Bypass	49 km as reported by FMW	Kano State	Ongoing construction by CCECC Continued under Tinubu; original award date not verified here Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
78	Kano-Jigawa / Kano-Maiduguri Section I corridor	100.9 km project length	Kano / Jigawa	Ongoing dualisation by Triacta Inherited; continued under Tinubu This is the Kano-Wudil-Shuwarin corridor, distinct from Kano-Tsalle-Hadejia. Avoid duplication with Kano-Maiduguri Section I. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
79	Malando-Ngaski-Wara-Auna rehabilitation	76.5 km project length	Kebbi / Niger border corridor	Rehabilitation began 28 January 2025; ongoing Commenced under Tinubu FMW 27 July 2025 gives rounded 76km. Also called Malando-Garin Baka-Ngaski-Wara. [source] Evidence: 2025-06-24 — thesun.ng	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
80	Nnamdi Azikiwe Way / Kaduna Western Bypass: Command Junction-Kawo	21.47 km dual carriageway (2026 report)	Kaduna State	Ongoing; accelerated since 2023 Inherited: awarded 2021; continued under Tinubu Scorecard states 21.447km; rounded 21.47km in 2026 report. Dangote tax-credit project. Evidence: 2026-05-01 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 118. Capture date may be earlier.
81	Kano-Kwanar Danja-Hadejia, Section II: Kano-Tsalle	82 km project length	Kano / Jigawa	Commissioned 31 May 2025; May 2024 scorecard photograph records earlier construction Inherited; continued under Tinubu Contract 7632; CCECC. Percentage is cumulative project completion, not Tinubu-only contribution. Commissioning confirmed by Presidency on 31 May 2025; length and historic picture remain from the May 2024 FMW scorecard. Evidence: 2025-05-31 — State House	 FMW scorecard, May 2024, PDF p. 115. Capture date may be earlier.
82	Kwanar Danja-Tsalle-Hadejia, Phase I / Tsalle-Hadejia section	117 km (scorecard: 117.037 km)	Jigawa; Gumel and Hadejia ends	About 75% complete; nearly 79 km reconstructed by January 2026 Inherited: awarded February 2022; continued under Tinubu Nearly 79km is reported reconstructed length, not an inferred 75% of contract length. Gerawa Global Engineering. Evidence: 2026-01-26 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 130. Capture date may be earlier.
83	Kunya-Kanya-Babura-Babban Mutum rehabilitation	47 km (scorecard: 47.51 km)	Jigawa State	82% complete; about 37 km rehabilitated by January 2026 Continued under Tinubu CRCC; full project not completed at source date. Evidence: 2026-01-26 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 128. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
84	Kano State border–Dutse–Kiyawa–Bauchi State border: special repairs	Not disclosed for repaired portions	Jigawa State	Completed December 2024; commissioned January 2026 New emergency intervention under Tinubu Commenced March 2024 under 260 emergency road projects; this is spot repair, not reconstruction of the entire corridor. Evidence: 2026-01-26 — Federal Ministry of Works	Verified segment photograph not available.
85	Ungwan Iliya Bagudu–Kwantakaran–Tsiga–Bakori, including Kadabo bridges	17 km plus three bridges	Kafur / Bakori, Katsina State	Ongoing; 11% controller estimate / 15.5% contractor estimate New: awarded February 2025 under Tinubu Conflicting same-day percentages are both disclosed; over 4km base course reported, not final completed road. Evidence: 2026-01-24 — Federal Ministry of Information	Verified segment photograph not available.
86	Kano–Katsina dualisation: Katsina/Kano border–Katsina Steel Rolling Mill Roundabout	Section length not disclosed in inspected source	Katsina State	Construction progressing at January 2026 inspection Continued under Tinubu; inherited project Do not substitute total Kano–Katsina corridor length for this specific contract section. Evidence: 2026-01-24 — Federal Ministry of Information	Verified segment photograph not available.
87	Katsina–Mararrabar Kankara: Mararraba–Tashan Boka–Gidan Daudu failed sections	Three interventions; lengths not disclosed	Katsina State	Emergency repairs completed and commissioned January 2026 New emergency interventions under Tinubu Evidence: 2026-01-24 — Federal Ministry of Information	Verified segment photograph not available.
88	Katsina–Dutsinma–Kankara: washouts at km1+775 and km2+736	Two locations; repaired length not disclosed	Katsina State	Emergency repairs completed and commissioned January 2026 New emergency interventions under Tinubu Chainages are locations, not work lengths. Evidence: 2026-01-24 — Federal Ministry of Information	Verified segment photograph not available.
89	Katsina–Daura: critical washout and bad-portion reinstatement	Not disclosed	Katsina State	Completed and commissioned January 2026 New emergency intervention under Tinubu Evidence: 2026-01-24 — Federal Ministry of Information	Verified segment photograph not available.
90	Mando–Birnin Gwari reconstruction	122 km contracted length	Kaduna State	Contract signed; contractor ordered to mobilise on 14 May 2026 Reconstruction contract awarded under Tinubu Approval/contract implementation milestone only; source does not establish physical completion or percentage. Evidence: 2026-05-14 — Federal Ministry of Works	Verified segment photograph not available.
91	Kano–Gwarzo–Dayi reconstruction	Length not stated in current source	Kano / Katsina	Ongoing project received renewed funding in 2026 Inherited: flagged off June 2021; continued under Tinubu Funding allocation is not evidence that entire corridor is complete. Evidence: 2026-04-30 — arise.tv	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
92	Maiyama road construction	3 km	Maiyama, Kebbi State	100% completed in May 2024 scorecard Federal construction delivered during Tinubu reporting period; award date not verified Contract 7869; Nextel Consulting. Evidence: 2024-05 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 120. Capture date may be earlier.
93	Yakasai-Badume-Damargu-Marken Zalli, with FCE Bichi spur	38.7 km project length	Kano State	Commissioned 31 May 2025; May 2024 scorecard photograph records earlier construction Continued under Tinubu Contract 6903; CCECC; chainage 15+320-27+330 completed to wearing course. Commissioning confirmed by Presidency on 31 May 2025; length and historic picture remain from the May 2024 FMW scorecard. Evidence: 2025-05-31 — State House	 FMW scorecard, May 2024, PDF p. 102. Capture date may be earlier.
94	Funtua-Dayi-Yashe bridge-embankment washout repairs	0.2 km intervention	Katsina; km79+000 -79+200	100% completed in May 2024 scorecard Emergency repair during Tinubu reporting period Contract 8313; Epsilon Sky. Evidence: 2024-05 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 124. Capture date may be earlier.
95	Sokoto-Talata Mafara: emergency failed-section repairs	0.65 km intervention	Sokoto; works within km40+300-42+000 corridor	100% completed in May 2024 scorecard Emergency repair under Tinubu Contract 8327; repair activity on corridor also undergoing dualisation. Do not add as new route length. Evidence: 2024-05 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 111. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
96	Kwasara-Behindi rehabilitation	5 km	Kebbi State	100% completed in May 2024 scorecard Federal rehabilitation during Tinubu reporting period; award date unverified Contract 7881; Fiserv International. Evidence: 2024-05 — Federal Ministry of Works	 Jan 14, 2024 1:34:44 PM 11.4879N 4.1687E Kwasara - Behinde road in Kebbi S FMW scorecard, May 2024, PDF p. 132. Capture date may be earlier.
97	Kwanar Garko-Garko-Kibiya: washouts and culvert-location repairs	0.3 km intervention; three culvert locations	Kano State	100% completed in May 2024 scorecard Emergency repairs under Tinubu Energyview Nigeria; spot repairs rather than full-corridor reconstruction. Evidence: 2024-05 — Federal Ministry of Works	 Garko, Kano, Nigeria Garko-Sumaila Rd, Garko 712101, Kano, Nigeria Lat 11.642033° Long 8.799435° 09/05/24 04:28 PM GMT +01:00 FMW scorecard, May 2024, PDF p. 134. Capture date may be earlier.
98	Gwiwa Low Cost-Mangoro road maintenance	Not disclosed	Sokoto State	Maintenance/repairs shown completed in before-and-after record FERMA intervention during Tinubu reporting period Before-and-after photos; no road length stated. Evidence: 2024-05 — Federal Ministry of Works	 268F4J9, opp. Binji Pharmacy, Mabera Mujaya, Sokoto 840103, Sokoto, Nigeria FMW scorecard, May 2024, PDF p. 260. Capture date may be earlier.
99	Farin Ruwa-Tsanyawa rehabilitation	Not disclosed	Kano State	Rehabilitation shown in before-and-after record FERMA intervention during Tinubu reporting period No completion percentage or length stated; limited to depicted intervention. Evidence: 2024-05 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 261. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
100	Dimurkol area spur to Daura-Kongolom: carriageway, culvert and lined drain	Not disclosed	Katsina State	Rehabilitation shown in before-and-after record FERMA intervention during Tinubu reporting period No project length stated. Evidence: 2024-05 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 262. Capture date may be earlier.
101	Malumfashi-Kafur-Dabai: general maintenance at km15-45	Within 30 km corridor; actual repaired length undisclosed	Katsina State	Maintenance shown in before-and-after record FERMA intervention during Tinubu reporting period 30km is chainage coverage, not 30km of newly constructed or continuously resurfaced road. Evidence: 2024-05 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 263. Capture date may be earlier.
102	Kaduna-Kachia-Gimi: retaining wall and eroded-section reinstatement	Spot intervention at km118+800; length undisclosed	Kaduna State	Rehabilitation shown in before-and-after record FERMA intervention during Tinubu reporting period Chainage is location, not length. Evidence: 2024-05 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 265. Capture date may be earlier.
103	Kalgo-Bunza-Kamba-Peka-Niger border: dangerous-pothole patching	Within km0-26.236; actual patched length undisclosed	Kebbi State	Emergency patching shown in before-and-after record FERMA intervention during Tinubu reporting period 26.236km is corridor inspected/covered, not continuous reconstruction. Evidence: 2024-05 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 266. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
104	Birnin Kebbi-Argungu-Sokoto border: dangerous-pothole patching	Within km8.5-70; actual patched length undisclosed	Kebbi State	Emergency patching shown in before-and-after record FERMA intervention during Tinubu reporting period Do not count 61.5km chainage span as fully resurfaced road. Evidence: 2024-05 — Federal Ministry of Works	
105	Gusau-Talata Mafara-Sokoto border: critical-pothole patching	Within km0-36.5; actual patched length undisclosed	Zamfara State	Emergency patching shown in before-and-after record FERMA intervention during Tinubu reporting period Shares corridor with dualisation; maintenance activity, not additional new route length. Evidence: 2024-05 — Federal Ministry of Works	
106	Gusau Bypass rehabilitation	Not disclosed	Zamfara State	Rehabilitation shown in before-and-after record FERMA intervention during Tinubu reporting period No measured length or project percentage supplied. Evidence: 2024-05 — Federal Ministry of Works	
107	Dumbulun-Tsanyawa Road (FERMA rehabilitation)	Not disclosed	Kano State	Rehabilitation documented with before-and-after photographs in the May 2023-May 2024 scorecard Federal road maintenance implemented under Tinubu (FERMA) No length or exact completion date stated; before photograph dated 9 November 2023. The after photograph shows the treated segment, not its 2026 condition. Evidence: 2024-05 — Federal Ministry of Works	

FMW scorecard, May 2024, PDF p. 267. Capture date may be earlier.

FMW scorecard, May 2024, PDF p. 268. Capture date may be earlier.

FMW scorecard, May 2024, PDF p. 269. Capture date may be earlier.

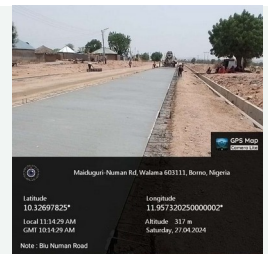
FMW scorecard, May 2024, PDF p. 259. Capture date may be earlier.

North-Central and North-East

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
108	Bida-Lapai-Lambata road reconstruction	124.88 km stated contract length	Niger	Ongoing in May 2024; further concrete reconstruction approved in February 2026 Inherited; awarded May 2018 Scorecard inconsistently prints 124.81/124.88/124.8 km; 79.3 km reported achieved is cumulative, not all since 2023. New approval covers 123.5 km: [source] (27 February 2026). Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
109	Ilorin-Jebba dualisation, Section I	110.8 km contract	Kwara	Ongoing; 65.8 km reported achieved cumulatively Inherited; awarded July 2018 2024 scorecard photograph on following page is headed Jebba-Mokwa; omitted to avoid mislabelling. Evidence: 2024-05-27 — Federal Ministry of Works	Verified segment photograph not available.
110	Jebba-Mokwa-Bokani Junction dualisation, Section II	46 km contract	Niger	Ongoing; 14.6 km reported achieved cumulatively Inherited; awarded July 2018 Contract length, not kilometres completed under Tinubu. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
111	Keffi-Akwanga-Lafia-Makurdi dualisation	221.8 km described; rounded 222 km in project field	Nasarawa and Benue	Reported completed in 2024 scorecard Inherited; contract 2018, works began April 2019 The related 5.4 km Abuja-Keffi expansion is a separate component. Do not add it again if listed under FCT. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
112	Suleja-Minna dualisation, Phase I (Diko Junction-Bonu)	40 km contract	Niger	Ongoing; 36 km reported achieved cumulatively Inherited; project predates 2023 Scorecard contains inconsistent award/start dates and completion percentage; those fields are not repeated here. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
113	Barkin Ladi-Pankshin road: flood intervention and lined drainage	0.630 km intervention	Plateau	Reported completed New; awarded January 2024; began February 2024 Local intervention, not rehabilitation of the entire corridor. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.


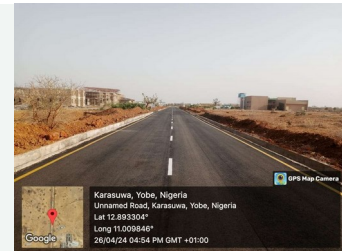
S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
114	Cham-Numan section of Gombe-Yola road rehabilitation	46.35 km contract	Gombe and Adamawa	Ongoing; contractor on site Inherited; Contract 6300 Photo is a completed/marked segment; overall corridor remained under construction in the source. Evidence: 2024-05-27 — Federal Ministry of Works	FMW scorecard, 2024; road segment shown after works or during construction.
115	Alkaleri-Futuk road rehabilitation	82 km contract	Bauchi	Ongoing; contractor on site Continued under Tinubu; inherited contract listed by ministry Evidence: 2024-05-27 — Federal Ministry of Works	FMW scorecard, 2024; road segment shown after works or during construction.
116	Kaleyeri-Damaturu road rehabilitation	54.50 km contract	Yobe	Ongoing; contractor mobilised Continued under Tinubu; inherited contract listed by ministry Evidence: 2024-05-27 — Federal Ministry of Works	FMW scorecard, 2024; road segment shown after works or during construction.


S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
117	Yola-Hong-Mubi road rehabilitation	185.5 km in project description; source length field inconsistent	Adamawa	Ongoing; contractor mobilised Inherited; Contract 6299 The same page's PROJECT LENGTH field says 46.35 km, apparently duplicated from Cham-Numan. Use 185.5 km only with this caveat; no silent correction. Evidence: 2024-05-27 — Federal Ministry of Works	
118	Biu-Numan road reconstruction, Section II (CH45+000-CH90+000)	45 km original section contract	Borno and Adamawa	Ongoing; contractor mobilised Inherited; Contract 7643 A July 2025 report describes an extension to 61.76 km on Biu-Numan, but section mapping is insufficiently clear to substitute it here. Evidence: 2024-05-27 — Federal Ministry of Works	
119	Damagum-Gubana road, Section II (CH5+650-CH8+650)	3.00 km section	Yobe	Reported completed Federal construction during Tinubu period; original award date not stated Evidence: 2024-05-27 — Federal Ministry of Works	

FMW scorecard, 2024; road segment shown after works or during construction.

FMW scorecard, 2024; road segment shown after works or during construction.

FMW scorecard, 2024; road segment shown after works or during construction.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
120	Bama-Banki road, critical intervention in Section I	1.150 km intervention	Borno	Reported completed Federal emergency work during Tinubu period Small intervention within a wider 49 km corridor. Overlaps the later full-road reconstruction; do not sum both as unique route kilometres. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
121	Yobe State University internal road, Damaturu	0.370 km intervention	Yobe	Reported completed Federal Ministry of Works intervention during Tinubu period Federal work on a state university road; not a state-funded presidential inauguration. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
122	Federal University Gashua internal road	0.470 km intervention	Yobe	Reported completed Federal Ministry of Works intervention during Tinubu period Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
123	Kaga-Gubio road, Section II (CH1+500-CH2+000)	0.500 km intervention	Borno	Reported completed Federal limited rehabilitation during Tinubu period Evidence: 2024-05-27 — Federal Ministry of Works	
124	Shendam Bridge on Shendam-Ibi road	0.060 km bridge	Plateau	Commissioned 31 May 2025; historic 2024 photograph shows works in progress Federal replacement/rehabilitation during Tinubu period Bridge length only. Source also describes about 80% of major bridge works; not a whole-road length. Evidence: 2025-05-31 — State House	
125	Bauchi-Kari-Yobe road: repair of damaged bridges (Contract 8131)	Repair length not stated; bridges along 176 km corridor	Bauchi	Bridge-repair package reported completed Federal repair works during Tinubu period 176 km is the corridor length, not the length repaired. Source heading says five bridges but names vary; retained as a single contract package. Evidence: 2024-05-27 — Federal Ministry of Works	



FMW scorecard, 2024; road segment shown after works or during construction.

FMW scorecard, 2024; road segment shown after works or during construction.

FMW scorecard, 2024; road segment shown after works or during construction.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
126	Bauchi-Jos road: repairs to six bridges	Repair length not stated; bridges along 120 km corridor	Bauchi	Bridge-repair package reported completed Federal repair works during Tinubu period Gada Biyu, Sabuwar Gada, Tsalle, Tilde, Narabi and Babale. Do not claim 120 km of new road. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
127	Abaji-Koton Karfe road: bridge intervention at CH103+515	0.080 km bridge	Kogi	Rehabilitation reported completed Federal intervention during Tinubu period Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
128	Obi-Aloshi-Benue State border road maintenance	Not stated for treated sections	Nasarawa	FERMA maintenance documented with before/after photographs FERMA works within May 2023–May 2024 reporting period Do not infer resurfacing of the entire route from a segment photograph. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
129	Ilorin-Igbetti-Oyo State border road: hydraulic structures	Works between CH1+300 and CH2+200; 0.9 km location range	Kwara	Drainage/hydraulic-structure rehabilitation documented FERMA works within May 2023–May 2024 reporting period 0.9 km is the chainage range containing structures, not necessarily continuously tarred road. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
130	Kainji Dam–New Bussa–Wawa road maintenance	Not stated for treated sections	Niger	Maintenance/rehabilitation documented with before/after photographs FERMA works within May 2023–May 2024 reporting period Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
131	Kabba–Isanlu–Irunda road maintenance	Not stated for treated sections	Kogi	Maintenance/repairs documented with before/after photographs FERMA works within May 2023–May 2024 reporting period Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
132	Heipang–Barkin Ladi–Mangu road maintenance	Not stated for treated sections	Plateau	Maintenance documented with before/after photographs FERMA works within May 2023–May 2024 reporting period Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
133	Gombe–Potiskum road maintenance	Not stated for treated sections	Gombe	Maintenance documented with before/after photographs FERMA works within May 2023–May 2024 reporting period Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
134	Gamawa–Udubo road maintenance (R333/F13)	Not stated for treated sections	Bauchi	Maintenance documented with before/after photographs FERMA works within May 2023–May 2024 reporting period Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
135	Numan–Mayolope road: direct-labour works	Not stated for treated sections	Adamawa	Direct-labour repairs documented with before/after photographs FERMA works within May 2023–May 2024 reporting period Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
136	Potiskum-Kari-Bauchi State border road maintenance	Not stated for treated sections	Yobe	Major maintenance and repairs documented FERMA works within May 2023–May 2024 reporting period Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
137	Biu-Shaffa-Garkida road: FERMA rehabilitation	Not stated for treated sections	Borno	Rehabilitation documented with before/after photographs FERMA works within May 2023–May 2024 reporting period Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
138	Jalingo-Mutum Biyu-Benue State border road: emergency repairs	0.500 km chainage span (KM87+000–KM87+500)	Taraba	Failed-segment repairs documented with before/after photographs FERMA works within May 2023–May 2024 reporting period Source says failed segmented sections within this span, not necessarily a continuous 0.5 km reconstruction. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, 2024; road segment shown after works or during construction.
139	Bama-Banki road reconstruction (Dangote tax-credit project)	49 km in July 2025 report; original chainage 49.153 km	Borno	Reported ongoing Inherited 2020 award; continued under Tinubu Separate from the 1.15 km completed emergency intervention on the same corridor; overlaps route kilometres. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
140	Dikwa-Gamboru-Ngala road reconstruction (Dangote tax-credit project)	51 km in July 2025 report; 49.577 km in 2024 contract schedule	Borno	Reported ongoing Inherited; continued under Tinubu The ministry's reports differ in length; figures preserved and not combined. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
141	Borno ring road (CCECC)	110 km stated project length	Borno	Reported under construction Federal project continued/constructed under Tinubu; original award date not verified Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
142	Makurdi-Otukpo-9th Mile dualisation	250 km route length in cited report	Benue and Enugu	Reported ongoing Inherited; continued under Tinubu 250 km dualised is not 500 km of unique road; other official summaries round this corridor to 260 km. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
143	Lokoja-Okene dualisation (CGC)	86 km route length in cited report	Kogi	Reported ongoing Inherited; continued under Tinubu Do not add a separate Obajana-Okene subsection without excluding overlap. Two carriageways do not create 172 km of unique route. Evidence: 2025-07-27 — Federal Ministry of Works	Verified segment photograph not available.
144	Akwanga-Kaduna-Jos superhighway section	125 km section	Nasarawa, Kaduna and Plateau	Flagged off / commencement announced 1 July 2026 New phased legacy-project delivery under Tinubu; earlier corridor proposal predates him State House describes this section as Akwanga-Kaduna-Jos. The whole corridor is described as 700 km although its five listed lengths total 735 km; do not sum them without clarification. Evidence: 2026-07-01 — State House	Verified segment photograph not available.
145	Gombe-Biu highway reconstruction and dualisation	125 km section	Gombe and Borno	Flagged off 4 June 2026; commencement reported Earlier road contracts inherited; new dualisation relaunched under Tinubu This is one section of the broader Akwanga-Maiduguri corridor. No completed kilometres claimed. Evidence: 2026-06-06 — punchng.com	Verified segment photograph not available.
146	Trans-Sahara Trade Route, Benue section	Benue section length not stated	Benue	Mobilisation reported ongoing New legacy-project execution under Tinubu Wider route links Calabar-Ebonyi-Benue-Kogi-Nasarawa-Abuja. Mobilisation does not establish completed pavement. Evidence: 2026-07-01 — State House	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
147	Bauchi–Jigawa road: failed-section interventions	Not stated for treated sections	Bauchi and Jigawa	Contractor mobilised and works reported ongoing Emergency federal repairs under Tinubu Triacta identified as contractor. Not a claim that the entire corridor is reconstructed. Evidence: 2026-09-09 — Federal Ministry of Works	Verified segment photograph not available.
148	Jimeta Bridge rehabilitation, Yola	Bridge / repair length not stated in verified source	Adamawa	Commissioned 31 May 2025 Federal bridge intervention completed and commissioned under Tinubu; original award date not verified Presidency names Jimeta Bridge in the North-East commissioning list. Do not attribute construction of the original historical bridge to Tinubu. Evidence: 2025-05-31 — State House	Verified segment photograph not available.
149	Murtala Mohammed Bridge rehabilitation at Koton Karfe	2 km bridge length per carriageway; not 4 km of unique route	Kogi	92% cumulative completion reported May 2024; underwater and substructure repairs, joints and Lokoja-bound overlay completed Inherited bridge rehabilitation continued under Tinubu; original bridge dates to the 1970s Contract 6708, Hallekem. Photograph timestamp reads 7 June 2023; does not establish how much work occurred after inauguration. This is bridge repair within Abuja–Lokoja corridor. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW archival photograph; timestamp 7 June 2023; bridge repair segment.
150	Abuja–Lokoja road: ongoing road contracts and emergency interventions	Road-contract lengths not stated in September 2026 update	FCT and Kogi	Several road contracts ongoing; three further critical sections at emergency procurement stage Inherited federal corridor continued under Tinubu; emergency packages added Corridor-level umbrella record, overlapping the separately identified Abaji–Koton Karfe and Murtala Mohammed Bridge interventions. Do not count as additional unique route kilometres or a distinct extra road; three sections in procurement are not claimed built. Evidence: 2026-09-09 — Federal Ministry of Works	Verified segment photograph not available.

Federal Capital Territory

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
151	Arterial Road N20 (Wole Soyinka Way), Northern Parkway–Outer Northern Expressway, including interchange bridges	3.5	Mabushi/ Katampe/Jahi/ Kado, Abuja	Road commissioned 4 June 2024; interchange bridges commissioned 25 June 2025 Inherited (awarded 2020) 3.5 km reported in 2024 commissioning title. The 2025 bridges are part of the same contract; listed together to avoid counting them as another road. Evidence: 2025-06-25 — FCTA / Abuja Digest; Additional source	 FCTA / Abuja Digest, 2024-06. Capture date not independently verified.
152	Inner Southern Expressway extension (Goodluck Ebele Jonathan Way): OSEX–Southern Parkway	3.5	Central/southern Abuja	Commissioned 5 June 2024 Inherited (awarded January 2010) Length reported in source title. Not the separate ISEX II project still ongoing in 2026. Evidence: 2024-06-05 — FCTA / Abuja Digest	Verified segment photograph not available.
153	Outer Southern Expressway: Villa Roundabout–Ring Road I junction	6.7	Abuja city centre– Apo axis	Commissioned 3 June 2024 Inherited (awarded about 2013) 6.7 km is the commissioned segment. A separate 2026 source describes the entire planned OSEX corridor as 67 km; do not substitute that corridor length. Evidence: 2024-06-03 — FCTA / Abuja Digest; Additional source	 FCTA / Abuja Digest, 2024-06. Capture date not independently verified.
154	Southern Parkway: National Christian Centre–Ring Road I	Not disclosed in cited source	Central Area/Garki, Abuja	98% complete at 28 April 2024 inspection Inherited; resumed under Tinubu Included as continued construction. This evidence establishes near completion, not a commissioning date. Evidence: 2024-04-28 — FCTA / Abuja Digest; Additional source	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
155	B6 and B12 / Constitution Avenue and Independence Avenue completion package	Not disclosed in cited source	Central Business District, Abuja	Commissioned 6 June 2024 Inherited (awarded 2007) Combined contract retained as one package; segment length not disclosed in cited commissioning report. Evidence: 2024-06-06 — FCTA / Abuja Digest	Verified segment photograph not available.
156	Wuye District internal road network and Wuye–Wuse interchange	37.5	Wuye, Abuja	Infrastructure commissioned in May 2024; further district commissioning 21 October 2025 Inherited (awarded 2009) 37.5 km is the district network package, not 37.5 km newly laid since 2023. Includes arterial, connector and local streets. 2024 and 2025 reports consolidated to avoid double counting. Evidence: 2025-10-21 — FCTA / Abuja Digest; Additional source	 FCTA / Abuja Digest, 2024-05. Capture date not independently verified.
157	Guzape District road infrastructure (Lots I and II; road named for Chinua Achebe)	Not disclosed in cited source	Guzape, Abuja	Commissioned June 2024 Inherited (awarded 2003) Cited report does not disclose a defensible segment length. Do not treat the naming as a separate road project. Evidence: 2024-06-08 — FCTA / Abuja Digest	 FCTA / Abuja Digest, 2024-06. Capture date not independently verified.
158	Ladi Kwali Road: Kwali town–Abuja –Lokoja highway	3.2	Kwali Area Council, FCT	Commissioned 11 June 2024 Inherited; long-abandoned road and bridge completed Includes associated bridge; source says road abandoned over 14 years and bridge 20 years. Evidence: 2024-06-11 — FCTA / Abuja Digest	 FCTA / Abuja Digest, 2024-06. Capture date not independently verified.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
159	Paikon Kore-Ibwa Road	9	Gwagwalada Area Council, FCT	Commissioned January 2025 New emergency-road programme Official sources conflict: February 2024 flag-off and June 2025 recap say 9 km; January commissioning article says 19 km. Use 9 km as repeatedly reported scope, with discrepancy disclosed. Evidence: 2025-06-23 — FCTA / Abuja Digest; Additional source; Additional source	 FCTA / Abuja Digest, 2025-01. Capture date not independently verified.
160	Gaba-Tokulo Road and bridge	5	Bwari Area Council, FCT	Commissioned 24 January 2025 New emergency-road programme Commissioning account says 5 km; February 2024 flag-off said 7.2 km. Scope discrepancy remains unresolved; do not count the two lengths separately. Evidence: 2025-01-24 — FCTA / Abuja Digest; Additional source; Additional source	 FCTA / Abuja Digest, 2025-01. Capture date not independently verified.
161	Garage Junction-LEA Secretariat township road	5	Kuje Area Council, FCT	Commissioned 23 January 2025 New rehabilitation/dualisation under Tinubu Road package reported as 5 km asphalt carriageway; separate from later LEA Secretariat-Kiyi extension. Evidence: 2025-01-23 — FCTA / Abuja Digest	 FCTA / Abuja Digest, 2025-01. Capture date not independently verified.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
162	Yangoji-Sukuku-Ebo (Ebbo) Road	11	Kwali Area Council, FCT	Commissioned 21 January 2025 New emergency-road programme Place names vary slightly across official accounts. Evidence: 2025-01-21 — FCTA / Abuja Digest; Additional source	 FCTA / Abuja Digest, 2025-01. Capture date not independently verified.
163	Saburi I and II access road	5	Abuja Municipal Area Council, FCT	Commissioned 25 January 2025 New emergency-road programme Separate from later Old Keffi Road/Kado-Dei-Dei rehabilitation. Evidence: 2025-01-25 — FCTA / Abuja Digest; Additional source	 FCTA / Abuja Digest, 2025-01. Capture date not independently verified.
164	Naharati-River Ukyu-Unguwan Hausawa Road	5	Abaji Area Council, FCT	Commissioned 20 January 2025 New emergency-road programme Includes river crossing infrastructure; official flag-off report was February 2024. Evidence: 2025-01-20 — FCTA / Abuja Digest; Additional source	 FCTA / Abuja Digest, 2025-01. Capture date not independently verified.
165	A2 Abuja-Lokoja highway junction-Pai Road	15	Kwali Area Council, FCT	Commissioned June 2025 New (awarded September 2024) Report published 23 June 2025 contains an inconsistent event date of Monday 24 June; month/year used. Excludes the proposed wider 45 km Pai-Gomani-Yangoji network. Evidence: 2025-06-23 — FCTA / Abuja Digest	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
166	Kabusa-Ketti access road	10	Abuja Municipal Area Council, FCT	Commissioned 27 June 2025 New (awarded November 2024) Technical commissioning brief gives 10 km asphalt single carriageway; flag-off title gave 10.5 km. Commissioned scope used. Evidence: 2025-06-27 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
167	Kabusa-Takushara Road	9.8	Abuja Municipal Area Council, FCT	Construction flagged off 3 December 2024; included in May 2025 proposed commissioning list New 9.8 km from flag-off report. Another article says 9.5 km; no completion assumed solely from proposed commissioning list. Evidence: 2024-12-03 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
168	Giri District access road	3	Giri, FCT	Commissioned 30 June 2025 New (awarded November 2024) Technical brief: 3 km asphalt-paved dual carriageway. Evidence: 2025-06-30 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
169	Ushafa-War College-Army Checkpoint road and connecting roads	16.4	Bwari Area Council, FCT	Commissioned 2 July 2025 New dualisation/upgrade under Tinubu 16.4 km is the package/network length, including connecting roads. Evidence: 2025-07-02 — FCTA / Abuja Digest	Verified segment photograph not available.
170	Aguma Palace-Radio Nigeria-New Market Road network	10	Gwagwalada Area Council, FCT	Commissioned 4 July 2025 New rehabilitation under Tinubu 10 km network including accompanying engineering services and streetlights. Evidence: 2025-07-04 — FCTA / Abuja Digest	Verified segment photograph not available.
171	Arterial Road N16: Ring Road I/Nicon junction-Arterial Road N20	3.7	Katampe, Abuja	Commissioned 11 June 2025 New (awarded October 2024) Official technical brief gives approximately 3.7 km including two interchanges. Initially described as Shehu Shagari Way; later sources call this Yemi Osinbajo Way. These are not separate roads. Evidence: 2025-06-11 — FCTA / Abuja Digest	Verified segment photograph not available.
172	Collector Road CN2 / Zakari Kyari Street: N11 (Ahmadu Bello Way)-Katampe, and connecting roads	Not disclosed in cited source	Mabushi/Katampe, Abuja	Commissioned 19 June 2025 New (awarded September 2024) Exact commissioned length not disclosed. Different segment from CN2 N16-N20 commissioned in 2026. Evidence: 2025-06-19 — FCTA / Abuja Digest	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
173	Collector Road CN8 / Asuquo Okon Street and connecting roads	Not disclosed in cited source	Dakibiyu, Abuja	Commissioned 1 July 2025 New (awarded September 2024) Six-lane main road with two-lane connecting roads; numerical length not disclosed. Evidence: 2025-07-01 — FCTA / Abuja Digest	Verified segment photograph not available.
174	Arterial Road N5 / Obafemi Awolowo Way: Life Camp Junction–Ring Road III	Not disclosed in cited source	Gwarinpa I/Dape, Abuja	Gwarinpa portion commissioned June 2025; Dape portion commissioned 10 June 2026 New (awarded September 2024) Two commissioning phases consolidated as one corridor/package. Length not disclosed in cited technical accounts. Evidence: 2026-06-10 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
175	Outer Southern Expressway left-hand service carriageway: Ring Road I–Wasa Junction	15	Apo–Wasa, Abuja	Commissioned 13 June 2025 New phase of inherited expressway (work started November 2024) Service carriageway scope, not the full planned ten-lane expressway. Main-carriageway work overlaps this corridor and must not be added as unique route-km. Evidence: 2025-06-13 — FCTA / Abuja Digest	Verified segment photograph not available.
176	Inner Northern Expressway right-hand service carriageway: Ring Road III–Outer Northern Expressway	Not disclosed in cited source	Idu/Gwagwa/Karimo/Jiwa–Zuba corridor, FCT	Commissioned 24 June 2025 Inherited (awarded December 2014) Report gives 32.5 km for the overall expressway, not a clearly segregated length for this commissioned service-carriageway phase. Length withheld to avoid overstating completed distance. Evidence: 2025-06-24 — FCTA / Abuja Digest	Verified segment photograph not available.
177	Kwaita–Yebu Road reconstruction	25	Kwali Area Council, FCT	Groundbreaking July 2024; construction inspected November 2024 New reconstruction phase under Tinubu 25 km contract scope. No completion inferred from the announced one-year target. Evidence: 2024-11-21 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
178	Nyanya–Karu–Orozo/Karshi Road rehabilitation	18	Eastern FCT/Abuja Municipal Area Council	Rehabilitation underway September 2024; listed for commissioning June 2025 New rehabilitation approved under Tinubu Official source alternates Nyanya–Karu–Orozo and Nyanya–Karshi. No completion assumed from proposed ceremony list. Evidence: 2024-09-26 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
179	Old Ushafa–Lower Usuma Dam Road rehabilitation	7.4	Bwari Area Council, FCT	Listed for forthcoming commissioning in June 2025 Rehabilitation under Tinubu; original award unclear Specific completion/commissioning not independently established by cited report; length is reported project scope. Evidence: 2025-06-23 — FCTA / Abuja Digest	Verified segment photograph not available.
180	Dutse Junction–Bwari road resurfacing	Not disclosed in cited source	Bwari Area Council, FCT	Works inspected November 2024; intervention confirmed January 2025 Rehabilitation under Tinubu Numerical length not disclosed in cited reports. Evidence: 2025-01-24 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
181	Access roads to Abuja Rail Mass Transit stations	Not disclosed in cited source	Abuja rail-station catchments, FCT	Construction inspected 31 January 2024 Continued/new access works; individual origins unclear Grouped enabling-road package. Station-level lengths and names not enumerated in cited article; rail track distance excluded. Evidence: 2024-01-31 — FCTA / Abuja Digest	Verified segment photograph not available.
182	Federal Capital City road resurfacing programme: Garki, Wuse, Maitama, Asokoro and Gwarinpa I	Not disclosed in cited source	Abuja city districts	135-road programme launched September 2023; further 189-road programme February 2024; about 170 km resurfacing reported June 2024 New rehabilitation programme Counts represent programme announcements and may overlap. About 170 km is a reported aggregate, not a new-road total. Individual street names/lengths unavailable in cited primary sources. Do not add 135+189 as distinct verified roads. Evidence: 2024-06-05 — FCTA / Abuja Digest ; Additional source ; Additional source	Verified segment photograph not available.
183	Highway FCT 105: Airport Expressway–Kuje Township Junction	8.6	Kuje approach, FCT	Commissioned 11 June 2026 Inherited (awarded February 2022) Completed first phase is 8.6 km six-lane dual carriageway; full planned FCT 105 highway is about 76 km, not completed here. Evidence: 2026-06-11 — FCTA / Abuja Digest	Verified segment photograph not available.
184	Kuje–Gwagwalada Road, phase I: LEA Secretariat–Kiyi Village	7	Kuje Area Council, FCT	Commissioned 24 June 2026 New (awarded February 2025) Only 7 km phase I commissioned; not the whole Kuje–Gwagwalada corridor. Evidence: 2026-06-24 — FCTA / Abuja Digest	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
185	Jahi-Gwarinpa interchange at Arterial Road N16/Ring Road II	Not disclosed in cited source	Jahi/Gwarinpa, Abuja	Commissioned 25 June 2026 Inherited (awarded late previous administration) Interchange counted as a project without converting bridge lanes into route-km. Evidence: 2026-06-25 — FCTA / Abuja Digest	Verified segment photograph not available.
186	Bill Clinton Drive-Tungan Madaki access road	7	Airport/Tungan Madaki, FCT	Commissioned 18 June 2026 New access-road phase under Tinubu 7 km road, with 80 m bridge. 14 km drainage is not road length. Separate from Tungan Madaki-Zuba extension. Evidence: 2026-06-18 — FCTA / Abuja Digest	Verified segment photograph not available.
187	Tungan Madaki-Zuba access-road extension	Not disclosed in cited source	Airport hinterland–Abuja–Kaduna highway at Zuba, FCT	Flagged off July 2026; ongoing August 2026 New Latest cited inspection confirms works, with December 2026 target; no target treated as completion. Evidence: 2026-08-19 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
188	Collector Road CN2 / Emmanuel Ogala Boulevard: N16–N20, including ILS-5	3.9	Katampe, Abuja	Commissioned 19 June 2026 New (awarded November 2025) Approximately 3.9 km package includes CN2 six-lane road plus ILS-5 four-lane street. Different segment from June 2025 CN2 commissioning. Evidence: 2026-06-19 — FCTA / Abuja Digest	Verified segment photograph not available.
189	Akinwumi Ajibola Street and ILS 16, 18 and 19 network	Not disclosed in cited source	Gaduwa, Abuja	Commissioned 1 July 2026 Road network delivered under Tinubu; original award unclear Package names confirmed; length not disclosed. Evidence: 2026-07-01 — FCTA / Abuja Digest	Verified segment photograph not available.
190	Karu Interchange–Customs Clinic Junction and adjoining township roads	5.4	Karu, Abuja Municipal Area Council	Commissioned 29 June 2026 New reconstruction (awarded August 2025) 5.4 km relates to principal dual carriageway in flag-off report. Adjoining DSS/NIA/EFCC/Hospital/Old CBN Quarters roads are additional package elements, without segregated lengths. Evidence: 2026-06-29 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
191	Collector Roads 01 and 02, Mabushi	Not disclosed in cited source	Mabushi, Abuja	Commissioned 26 June 2026 New works under Tinubu; precise award origin unclear Length not disclosed. Separate from the Esther Bali/Kez Udezue streets commissioned October 2025. Evidence: 2026-06-26 — FCTA / Abuja Digest	Verified segment photograph not available.

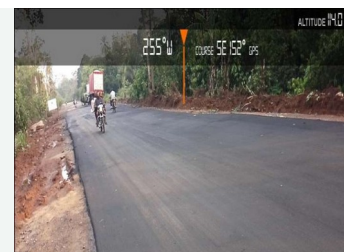
S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
192	Renewed Hope City access-road network: N11, N16, N40/M40 and SILS 03	10.5	Karsana West, FCT	Commissioned 3 July 2026 New (awarded February 2025) 10.5 km network total. Source components: 4.37, 2.75, 2.2 and approximately 1.1 km; rounding differs. Road code rendered N40 in flag-off and M40 in commissioning; one network counted. Evidence: 2026-07-03 — FCTA / Abuja Digest; Additional source	Verified segment photograph not available.
193	Old Keffi Road / Kado Village–Dei-Dei Junction rehabilitation	15	Kado/Karmo–Dei-Dei, FCT	Commissioned 2 July 2026 New rehabilitation under Tinubu 15 km asphalt rehabilitation with drainage and lighting; distinct from Saburi access road. Evidence: 2026-07-02 — FCTA / Abuja Digest; Additional source	Verified segment photograph not available.
194	Kaba–Kagini–Zaudna Road	Not disclosed in cited source	Kaba/Kagini/Zaudna, FCT	Award announced July 2026; project inspected August 2026 New July source ordered mobilisation; August inspection provides evidence beyond award alone. Length not disclosed. Evidence: 2026-08-20 — FCTA / Abuja Digest; Additional source	Verified segment photograph not available.
195	Arab/Gbazango Road reconstruction	Not disclosed in cited source	Kubwa, Bwari Area Council	Commissioned 17 July 2026 New reconstruction under Tinubu Length not disclosed in commissioning account; unrelated total of 317 km satellite-town awards must not be assigned to this road. Evidence: 2026-07-17 — FCTA / Abuja Digest	Verified segment photograph not available.
196	Transitway N2: Constitution Avenue –Ahmadu Bello Way	Not disclosed in cited source	Central Business District–Wuse, Abuja	Commissioned 7 July 2026 New (awarded October 2025) Dual carriageway and two bridges. Median reserved for future rail; no rail length counted as road. Evidence: 2026-07-07 — FCTA / Abuja Digest	Verified segment photograph not available.
197	Collector Road C01 and bridge linking Body of Benchers, Nile University and Baze University	Not disclosed in cited source	Institution and Research District, Abuja	Commissioned 8 July 2026 New (flagged off October 2025) Length not disclosed. Separate from newly flagged six-kilometre extension to Ring Road III. Evidence: 2026-07-08 — FCTA / Abuja Digest; Additional source	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
198	Collector Road C01 extension: Nile University–Ring Road III, with Baze University–Nile dualisation	6	Institution and Research District, Abuja	Flagged off 23 June 2026; construction target January 2027 New 6 km stated project scope; do not describe as completed. Existing C01 segment is separately listed. Evidence: 2026-06-23 — FCTA / Abuja Digest	Verified segment photograph not available.
199	Wasa Informal Sector Layout access roads	Not disclosed in cited source	Wasa, FCT	Commissioned 10 July 2026 New enabling infrastructure under Tinubu Road works included within electricity/water/infrastructure package; road-only length not provided. A mentioned remaining 10 km is prospective, not completed. Evidence: 2026-07-10 — FCTA / Abuja Digest	Verified segment photograph not available.
200	Outer Southern Expressway main carriageways: Ring Road I–Ring Road II	4	Apo/Wasa corridor, Abuja	Commissioned June 2026 New main-carriageway phase of inherited corridor (awarded late 2025) Two main carriageways each 4 km: 4 route-km, not 8 route-km. Overlaps corridor of 15 km service carriageway listed separately. Article publication is 9 June but body mistakenly says 9 March; month follows dated commissioning series. Evidence: 2026-06-09 — FCTA / Abuja Digest	Verified segment photograph not available.
201	Southern Parkway service carriageways: Arterial Road S20–Ring Road II	3	Durumi/Gudu/Gaduwa/southern Abuja	Flagged off June 2026; works underway July 2026 New phase Two service carriageways about 3 km each: 3 route-km, not 6 route-km. Different package from National Christian Centre–RR1. Evidence: 2026-06-23 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
202	Apo–Karshi Road	13.25	Abuja Municipal Area Council, FCT	Ongoing at August 2026 inspection; December 2026 target Inherited (awarded 2010; terminated and re-awarded) Contract re-awarded to SCC. Target completion must not be presented as completed. Evidence: 2026-08-22 — FCTA / Abuja Digest	Verified segment photograph not available.
203	Bwari–Kubwa Road	14	Bwari Area Council, FCT	Ongoing August 2026; December 2026 target New (awarded 2025) Approximately 14 km stated in latest report. Evidence: 2026-08-22 — FCTA / Abuja Digest	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
204	Inner Southern Expressway phase II, first phase and two interchanges	5.4	Southern Abuja	Ongoing August 2026; December 2026 target Inherited (awarded 2014) Approximately 5.4 km current phase. Different from 3.5 km OSEX–Southern Parkway extension commissioned in 2024. Evidence: 2026-08-19 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
205	Arterial Road N16 full-scope development: Ring Road II–Ring Road III	Not disclosed in cited source	Gwarinpa/Karsana, Abuja	Ongoing July–August 2026 Continuation under Tinubu; initial award unclear Not the Katampe Ring Road I–N20 segment. Interchange at Ring Road II may be a related component; avoid summing associated bridge/corridor lengths. Evidence: 2026-07-29 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
206	Collector Road C01: Berger Clinic–Dape District	Not disclosed in cited source	Life Camp/Dape, Abuja	Ongoing August 2026; December target Works under Tinubu; original award unclear This C01 is in Life Camp, distinct from Institution and Research District C01. Evidence: 2026-08-22 — FCTA / Abuja Digest	Verified segment photograph not available.
207	Arterial Road N1: Wuye District–Ring Road II	Not disclosed in cited source	Wuye/Jabi/Utako/Dakibiyu, Abuja	Flagged off September 2025; ongoing August 2026 New Six-lane dual carriageway; length not disclosed in cited reports. Evidence: 2026-08-22 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.
208	Arterial Road N20 / Solomon Lar Way: N5–Airport Expressway	Not disclosed in cited source	Western Abuja/Kukwaba corridor	Flagged off 25 September 2025 New phase Source identifies N20/Solomon Lar Way. Distinct southern/western extension from N20/Wole Soyinka Way commissioned in 2024. Evidence: 2025-09-25 — FCTA / Abuja Digest	Verified segment photograph not available.
209	Esther Bali Street (ILS11) and Kez Udezue Street (MAR24)	Not disclosed in cited source	Mabushi, Abuja	Commissioned 16 October 2025 New (awarded about six months earlier) Two-street access/infrastructure package; length not disclosed. Evidence: 2025-10-16 — FCTA / Abuja Digest	Verified segment photograph not available.
210	Kaura District road near FCT Fire Station, with extension to Oladipo Diya Road	Not disclosed in cited source	Kaura, Abuja	Ongoing July 2026; extension directed Works under Tinubu; original award unclear Original section approaching bridge completed; whole project and newly directed extension not yet complete. Evidence: 2026-07-31 — FCTA / Abuja Digest	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
211	Gomani-Dafa-Yangoji Road	13	Kwali Area Council, FCT	Commissioned 30 June 2026 New (awarded November 2025) 13 km in final commissioning account; earlier June 2026 remarks called it 15 km. Commissioned figure used. Distinct from Yangoji-Sukuku-Ebo Road. Evidence: 2026-06-30 — FCTA / Abuja Digest ; Additional source	Verified segment photograph not available.

Federal agency interventions

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
212	Eket-Ikot Abasi Road — FERMA maintenance	Not stated	Akwa Ibom	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Selected maintenance works; road-wide reconstruction is not claimed. Evidence: 2024-05-27 — Federal Ministry of Works	
213	Opolo-Elebele-Emayal Road — carriageway maintenance	1.9 km intervention interval	Bayelsa	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Chainage 11+400–13+300; interval length, not total road length. Evidence: 2024-05-27 — Federal Ministry of Works	
214	Ikom-Wula-Obudu Road — major maintenance	Not stated	Cross River	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Selected maintenance works; no total repaired length published. Evidence: 2024-05-27 — Federal Ministry of Works	

FMW scorecard, May 2024, PDF p. 281. Capture date may be earlier.

FMW scorecard, May 2024, PDF p. 282. Capture date may be earlier.

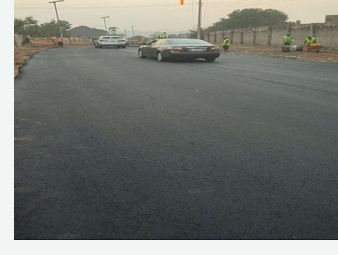
FMW scorecard, May 2024, PDF p. 283. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
215	Port Harcourt-Isiokpo-Elele-Omerelu-Imo border Road — pavement repairs	0.696 km intervention interval	Rivers	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Chainage 35+000-35+696; interval length, not entire corridor. Evidence: 2024-05-27 — Federal Ministry of Works	
216	Benin-Asaba-Onitsha dual carriageway — Niger Bridge-Edo border maintenance	Not stated	Delta	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration FERMA spot maintenance; distinguish from FMW reconstruction on the same corridor. Evidence: 2024-05-27 — Federal Ministry of Works	
217	Benin-Agbor-Asaba dual carriageway — Aduhanhan Bridge failed section	Not stated	Edo	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration At chainage 13+050, Agbor-bound; repairs to a failed section, not the whole road. Evidence: 2024-05-27 — Federal Ministry of Works	

FMW scorecard, May 2024, PDF p. 284. Capture date may be earlier.

FMW scorecard, May 2024, PDF p. 285. Capture date may be earlier.

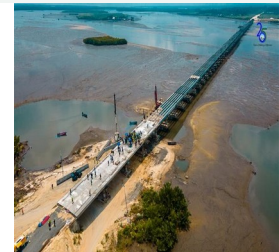
FMW scorecard, May 2024, PDF p. 286. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
218	Aba-Azumini Road — general maintenance	Not stated	Abia	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Route 409/F104; maintenance intervention. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 287. Capture date may be earlier.
219	Nnamdi Azikiwe University, Ifite Campus Road — major repairs	Not stated	Anambra	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration FERMA campus access-road maintenance. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 288. Capture date may be earlier.
220	Enugu-Abakaliki Road to Ebonyi border — major maintenance	Not stated	Enugu	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration FERMA maintenance, separate from wider road reconstruction. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 289. Capture date may be earlier.
221	Obiozara-Uburu-Mpu-Ishiagu-Enugu/Port Harcourt Expressway link — Amaeze Ishiagu section	Not stated	Ebonyi	Ongoing maintenance as at May 2024 Federal Roads Maintenance Agency (FERMA), Tinubu administration Source photograph labelled Ongoing, not After. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 290. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
222	Okposi-Nara-Enugu border Road — emergency maintenance	5.8 km intervention interval	Ebonyi	Ongoing maintenance as at May 2024 Federal Roads Maintenance Agency (FERMA), Tinubu administration Chainage 16+000–21+800; direct-labour works; source photograph labelled Ongoing. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 291. Capture date may be earlier.
223	Owerri-Obowo-Umuahia Road — Mile 7½ maintenance	Not stated	Imo	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Local maintenance at Mile 7½, not full corridor rehabilitation. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 292. Capture date may be earlier.
224	Western Avenue dual carriageway — general maintenance	Not stated	Lagos	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Route 20/A1; FERMA maintenance. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 293. Capture date may be earlier.
225	Okemesi-Ido-Ile Ekiti spur on Ado-Arakoko-Ilesha Road — repairs	Not stated	Ekiti	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Special maintenance repairs. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 294. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
226	Ibadan-Ife Road — Shasha II and III bridge maintenance	Not stated	Osun	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Bridge repairs at chainage 60+100, right and left carriageways; not road kilometres. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 295. Capture date may be earlier.
227	Sagamu Interchange-Papalanto Road — major maintenance	Not stated	Ogun	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Maintenance intervention; source spells Sagamu as Shagamu. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 296. Capture date may be earlier.
228	Owo-Ikare-Arigidi-Ekiti border Road — general maintenance	Not stated	Ondo	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Selected maintenance works. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 297. Capture date may be earlier.
229	Iseyin-Ipapo-Okaka-Alaga-Ago Are Road — general maintenance	Not stated	Oyo	Maintenance executed; before/after evidence in May 2024 scorecard Federal Roads Maintenance Agency (FERMA), Tinubu administration Selected maintenance works. Evidence: 2024-05-27 — Federal Ministry of Works	 FMW scorecard, May 2024, PDF p. 298. Capture date may be earlier.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
230	Obehie-Oke Ikpe Road	9	Ukwa West, Abia	Reconstructed; commissioned May 2024 NDDC federal intervention during Tinubu administration NDDC intervention; not the full Obehie-Azumini-Etim Ekpo corridor. Evidence: 2024-11-15 — NDDC	Verified segment photograph not available.
231	Iko-Atabrikang-Akata-Opulom-Ikot Inwang-Okoroutip-Iwuochang Road and Ibeno Bridge	6.87 road; 0.6 bridge	Ibeno, Akwa Ibom	Completed; commissioned May 2024 NDDC federal intervention during Tinubu administration 6.87 km pre-commissioning specification; later NDDC release rounds road to 6 km. Bridge is part of package, not extra independent road mileage. Completion corroborated by NDDC 15 November 2024 release. Evidence: 2024-05-18 — NDDC	Verified segment photograph not available.
232	Ndoro-Ntalakwu and adjoining roads	18.25	Ikwuano, Abia	Inherited 2019 contract completed; commissioned March 2025 NDDC federal intervention during Tinubu administration Engineering breakdown gives 18.25 km Ikwuano + 5.5 km Umuahia South = 23.75 km; do not count headline 23.7 km again. Evidence: 2025-03-14 — NDDC	Verified segment photograph not available.
233	Isi-Court-Olokoru-Amaoba Oboro road network	5.5	Umuahia South, Abia	Inherited 2019 contract completed; commissioned March 2025 NDDC federal intervention during Tinubu administration Separate 5.5 km component of the combined 23.75 km Abia package. Evidence: 2025-03-14 — NDDC	Verified segment photograph not available.
234	Abraka-Oben Road — first phase	9.6 reported by NDDC	Abraka, Ethiope East, Delta	First phase reconstructed and inaugurated February 2025 NDDC federal intervention during Tinubu administration Not the entire route into Edo. NDDC Edo commissioner clarified Orhionmwon section had not started (Punch, 8 March 2025; [source] that account says 9.8 km, unlike NDDC 9.6 km. Evidence: 2025-09-26 — NDDC	Verified segment photograph not available.
235	Oyigbo road network: Obunku-Umuosi-Obeakpu-Mgboji-Ndoki	7.3	Oyigbo, Rivers	Reconstructed; inaugurated 2025 NDDC federal intervention during Tinubu administration Network total. December 2024 inspection described 5.5 km; later inauguration reports 7.3 km. Evidence: 2025-09-26 — NDDC	Verified segment photograph not available.
236	Eziama-Abba-Owerre Nkworji Road	7.8	Isiala Mbano and Nwangele, Imo	Reconstructed; inaugurated 2025 NDDC federal intervention during Tinubu administration NDDC completed-road update. Evidence: 2025-09-26 — NDDC	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
237	Abraka-Agbor Road — NDDC reconstruction	Not stated	Delta	Reconstruction launched February 2025 NDDC federal intervention during Tinubu administration Flag-off verified; source does not establish completion or physical progress percentage. Evidence: 2025-09-26 — NDDC	Verified segment photograph not available.
238	Mgboji-Umuagbu-Akwete Road	Not stated	Rivers-Abia link, serving Akwa Ibom	Reconstruction launched 2025 NDDC federal intervention during Tinubu administration Road naming follows NDDC release; launch is not completion. Evidence: 2025-09-26 — NDDC	Verified segment photograph not available.
239	Bonny Ring Road and bridges	Not stated in cited progress source	Bonny, Rivers	Work continuing in 2025 NDDC federal intervention during Tinubu administration NDDC names active legacy project. July 2025 indexed NDDC release reports 27.14 km; omitted here pending durable article URL. Evidence: 2025-09-26 — NDDC	Verified segment photograph not available.
240	Okrika-Borikiri bridge and connecting road project	Not stated	Okrika-Port Harcourt, Rivers	Work continuing in 2025 NDDC federal intervention during Tinubu administration NDDC names active legacy project; completion not confirmed. Evidence: 2025-09-26 — NDDC	Verified segment photograph not available.
241	Kaa-Ataba Road and bridges	2 km road; main bridge 1.2 km	Khana and Andoni, Rivers	Inherited project resumed; ongoing, July 2026 report says nearing completion NDDC federal intervention during Tinubu administration NDDC reports 70% progress in December 2024; July 2026 progress corroboration: [source] Road and bridge quantities should not be added without scope clarification. Evidence: 2024-12-12 — NDDC	 Photograph in source dated 2024-12-12. Capture date not independently verified.
242	Benin-Sapele Expressway — NDDC emergency reconstruction	Not stated	Delta section	Contractors mobilised; reconstruction flagged off 28 August 2026 NDDC federal intervention during Tinubu administration NDDC intervention supervised by Federal Ministry of Works. May overlap FMW corridor entries; identify as specific emergency intervention, not an additional full road. Evidence: 2026-08-28 — NDDC	Verified segment photograph not available.

S/N	Road / project	Kilometres	Location	Work, attribution and dated evidence	Picture of road segment
243	Mutai-Ngalda Road	Not stated in cited progress source	Yobe	Inherited road project; construction ongoing June 2025 NEDC federal intervention during Tinubu administration Ministerial report records request to hasten ongoing construction. Historic reports vary between 54 and 55 km; no inferred length. Evidence: 2025-06-02 — Federal Ministry of Information	Verified segment photograph not available.
244	Ngwom-Mafa and Jere road network	Not stated	Mafa and Jere, Borno	Construction ongoing June 2025 NEDC federal intervention during Tinubu administration Ministerial report specifically identifies ongoing roads. Network retained as one package to avoid inventing road-by-road quantities. Evidence: 2025-06-02 — Federal Ministry of Information	Verified segment photograph not available.
245	Damaturu-Gujba-Buni Yadi-Magza Road — asphalt overlay	77 project; 25 phase I commenced	Yobe	Reconstruction launched; phase I physically commenced February 2026 NEDC federal intervention during Tinubu administration NEDC contractor mobilised for initial 25 km; 77 km is total planned corridor, not completed mileage. Evidence: 2026-02-19 — radionigerianortheast.gov.ng	Verified segment photograph not available.
246	Kara-Masaka-Mazaga community road and bridges	2.5 road package	Potiskum, Yobe	Sites handed over; construction launched January 2026 NEDC federal intervention during Tinubu administration Two bridges included in announced works, one serving Tandari; ten-month delivery period stated, not proof of completion. Evidence: 2026-01-23 — guardian.ng	Verified segment photograph not available.
